

# Work Order ID **94343**

December-10-12 12:36:21 PM

**\*94343\***

Page 1

Item ID: D206-667-247TRN

Accept

**\*N900040100\***

Setup Start **\*NS1\***

Revision ID:

Stop **\*NS2\***

Item Name: Crosstube Assembly, Mid Aft

Start Date: 10/12/2012 Start Qty: 1.00

**\*1\***

Cust Item ID:

Required Date: 24/12/2012 Req'd Qty: 1.00

**\*1\***

Customer:

Reference:

Approvals:

Process Plan: *MLJ*

Date: *12-12-10*

Tooling:

Date:

QC:

Date:

SPC (Y/N):

Date:

Run Start **\*NR1\***

Stop **\*NR2\***

| Sequence ID/<br>Work Center ID | Operation<br>Description | Set Up/<br>Run Hours | Tool ID | Tool # | Plan<br>Code | Accept<br>Qty | Reject<br>Qty | Reject<br>Number | Insp.<br>Stamp |
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|

| Draw Nbr     | Revision Nbr |
|--------------|--------------|
| D206-667-247 | A            |

100

0.00

**\*100\***

MORI SEIKI CNC LATHE LARGE

Mori Seiki

Memo

0.00

Mori Seiki CNC Lathe Large

1-Fill tube with sand & install plugs DTxxxx on both ends as per Folio FB030  
2-Turn first side as per Folio FB030  
3-File down transition lines smooth.  
FOLIO REV: *AA*  
DWG REV: *A*

*1 Ø* *MAN. L*  
*KC*  
*12/12/15*

110

QC1- Inspect dimensions to dimension sheet

0.00

**\*110\***

QC

Memo

0.00

Quality Control

*1 Ø* *MAN. L*  
*KC*  
*12/12/15*

NCR: Yes / No

**WORK ORDER NON-CONFORMANCE / UPDATE**

DQA: \_\_\_\_\_ Date: \_\_\_\_\_

QA Closed: \_\_\_\_\_ Date: \_\_\_\_\_

|  |   |   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____<br><br>Part No. _____<br><br>NCR No. _____ | <b>DISPOSITION</b><br><br>Rework <input type="checkbox"/><br>Scrap <input type="checkbox"/><br>Use-as-is <input type="checkbox"/><br>Work Order Update <input type="checkbox"/> | <b>AGAINST DEPARTMENT/PROCESS</b><br><br><table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/>   | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> |  |
| Skid-tube <input type="checkbox"/>                           | Crosstube <input type="checkbox"/>  | Water Jet <input type="checkbox"/>  | Engineering <input type="checkbox"/> |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Machining <input type="checkbox"/>                           | Small Fab <input type="checkbox"/>  | Prod. Eng. Coord. <input type="checkbox"/>  | Quality <input type="checkbox"/>     |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Thermoforming <input type="checkbox"/>                       | Finishing <input type="checkbox"/>  | Rec/Store/Packaging <input type="checkbox"/>  | Other <input type="checkbox"/>       |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Large Fab <input type="checkbox"/>                           | Composite <input type="checkbox"/>  | Supplier <input type="checkbox"/>   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |

| Root Cause    | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data      |      |      |     |   |                   |                    |             |              |              |
| Equip/Tooling |      |      |     |   |                   |                    |             |              |              |
| Operator      |      |      |     |   |                   |                    |             |              |              |
| Material      |      |      |     |   |                   |                    |             |              |              |
| Setup         |      |      |     |   |                   |                    |             |              |              |
| Other         |      |      |     |   |                   |                    |             |              |              |
| Process       |      |      |     |   |                   |                    |             |              |              |
| Supplier      |      |      |     |   |                   |                    |             |              |              |
| Training      |      |      |     |   |                   |                    |             |              |              |
| Unapproved    |      |      |     |   |                   |                    |             |              |              |

**FAULT CATEGORY**

| Landing Gear  | General                                 | Other  |
|---|---|--|
| <input type="checkbox"/> Bending                      | <input type="checkbox"/> Bend           | <input type="checkbox"/> Grain                           |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route      | <input type="checkbox"/> Hardware                        |
| <input type="checkbox"/> Cracks                       | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete           |
| <input type="checkbox"/> Crushed/Crimped              | <input type="checkbox"/> Burrs          | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs                        | <input type="checkbox"/> Contamination  | <input type="checkbox"/> Maintenance                     |
| <input type="checkbox"/> Heat Treat                   | <input type="checkbox"/> Countersink    | <input type="checkbox"/> Mislabeled                      |
| <input type="checkbox"/> Inspection Strip in Tube     | <input type="checkbox"/> Cut Too Short  | <input type="checkbox"/> Misread                         |
| <input type="checkbox"/> Ripples in Bend              | <input type="checkbox"/> Drill Holes    | <input type="checkbox"/> Offset                          |
| <input type="checkbox"/> Torque Waves in Extrusion    | <input type="checkbox"/> Drawing        | <input type="checkbox"/> Out of Calibration              |
| <input type="checkbox"/> Turning Sequence             | <input type="checkbox"/> Finish         | <input type="checkbox"/> Out of Sequence                 |
| <input type="checkbox"/> Wave/Twist in Tube           | <input type="checkbox"/> Folio          | <input type="checkbox"/> Outside Dimensions              |
|   |   | <input type="checkbox"/> Ovalized                        |
|   |   | <input type="checkbox"/> Over/Under tolerance            |
|   |   | <input type="checkbox"/> Part Incorrect                  |
|   |   | <input type="checkbox"/> Part Lost/Missing               |
|   |   | <input type="checkbox"/> Part Moved                      |
|   |   | <input type="checkbox"/> Positioned Wrong                |
|   |   | <input type="checkbox"/> Power Loss/Surge                |
|   |   | <input type="checkbox"/> Pressure/Forced                 |
|   |   | <input type="checkbox"/> Temperature/Cure                |
|   |   | <input type="checkbox"/> Weld                            |
|   |   | <input type="checkbox"/> Wrong Stock Pulled              |
|   |   | <input type="checkbox"/> Other                           |

# Work Order ID 94343

December-10-12 12:36:21 PM

**\*94343\***

Page 2

Item ID: D206-667-247TRN

Accept

**\*N900040100\***

Setup Start **\*NS1\***

Revision ID:

Stop **\*NS2\***

Item Name: Crosstube Assembly, Mid Aft

Start Date: 10/12/2012 Start Qty: 1.00

**\*1\***

Cust Item ID:

Required Date: 24/12/2012 Req'd Qty: 1.00

**\*1\***

Customer:

Reference:

Approvals: Process Plan: \_\_\_\_\_ Date: \_\_\_\_\_ Tooling: \_\_\_\_\_ Date: \_\_\_\_\_

Run Start **\*NR1\***

QC: \_\_\_\_\_ Date: \_\_\_\_\_ SPC (Y/N): \_\_\_\_\_ Date: \_\_\_\_\_

Stop **\*NR2\***

| Sequence ID/<br>Work Center ID | Operation<br>Description  | Set Up/<br>Run Hours | Tool ID | Tool # | Plan<br>Code | Accept<br>Qty | Reject<br>Qty | Reject<br>Number | Insp.<br>Stamp                      |
|--------------------------------|---|----------------------|---------|--------|--------------|---------------|---------------|------------------|-------------------------------------|
| 120                            |   | 0.00                 |         |        |              |               |               |                  |                                     |
| <b>*120*</b>                   | MORI SEIKI CNC LATHE LARGE  |                      |         |        |              |               |               |                  |                                     |
| Mori Seiki                     | <b>Memo</b>   | 0.00                 |         |        |              |               |               |                  |                                     |
| Mori Seiki CNC Lathe Large     | 1-Turn second side as per Folio FB030<br>2-File down transition lines smooth.<br>3-Remove sand and plugs<br>FOLIO REV: <u>AA</u><br>DWG REV: <u>A</u> |                      |         |        |              |               |               |                  | <i>mmv</i><br><i>KC</i><br>12-12-15 |
| 130                            |   | 0.00                 |         |        |              |               |               |                  |                                     |
| <b>*130*</b>                   | QC1- Inspect dimensions to dimension sheet  |                      |         |        |              |               |               |                  |                                     |
| QC                             | <b>Memo</b>   | 0.00                 |         |        |              |               |               |                  |                                     |
| Quality Control                |   |                      |         |        |              |               |               |                  | <i>mmv</i><br><i>KC</i><br>12-12-15 |
| 140                            |   | 0.00                 |         |        |              |               |               |                  |                                     |
| <b>*140*</b>                   | QC8- Inspect parts - second check   |                      |         |        |              |               |               |                  |                                     |
| QC                             | <b>Memo</b>   | 0.00                 |         |        |              |               |               |                  |                                     |
| Quality Control                |   |                      |         |        |              |               |               |                  | <i>TW</i> 12-12-17                  |

*AA* 141  
12.12.18

Grind only transition lines  
smooth longitude way.

*Rm* 12.12.17

NCR: Yes / No

## WORK ORDER NON-CONFORMANCE / UPDATE

DQA: \_\_\_\_\_ Date: \_\_\_\_\_

QA Closed: \_\_\_\_\_ Date: \_\_\_\_\_

|  |   |   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____<br><br>Part No. _____<br><br>NCR No. _____ | <b>DISPOSITION</b><br><br>Rework <input type="checkbox"/><br>Scrap <input type="checkbox"/><br>Use-as-is <input type="checkbox"/><br>Work Order Update <input type="checkbox"/> | <b>AGAINST DEPARTMENT/PROCESS</b><br><br><table style="width: 100%; border: none;"> <tr> <td style="width: 33%;">Skid-tube <input type="checkbox"/></td> <td style="width: 33%;">Crosstube <input type="checkbox"/></td> <td style="width: 33%;">Water Jet <input type="checkbox"/></td> <td style="width: 33%;">Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/>   | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> |  |
| Skid-tube <input type="checkbox"/>                           | Crosstube <input type="checkbox"/>  | Water Jet <input type="checkbox"/>  | Engineering <input type="checkbox"/> |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Machining <input type="checkbox"/>                           | Small Fab <input type="checkbox"/>  | Prod. Eng. Coord. <input type="checkbox"/>  | Quality <input type="checkbox"/>     |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Thermoforming <input type="checkbox"/>                       | Finishing <input type="checkbox"/>  | Rec/Store/Packaging <input type="checkbox"/>  | Other <input type="checkbox"/>       |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Large Fab <input type="checkbox"/>                           | Composite <input type="checkbox"/>  | Supplier <input type="checkbox"/>   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |

| Root Cause                             | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Equip/Tooling <input type="checkbox"/> |      |      |     |   |                   |                    |             |              |              |
| Operator <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Material <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Setup <input type="checkbox"/>         |      |      |     |   |                   |                    |             |              |              |
| Other <input type="checkbox"/>         |      |      |     |   |                   |                    |             |              |              |
| Process <input type="checkbox"/>       |      |      |     |   |                   |                    |             |              |              |
| Supplier <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Training <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Unapproved <input type="checkbox"/>    |      |      |     |   |                   |                    |             |              |              |

### FAULT CATEGORY

|   |   |   |   |
|---|---|---|---|
| <b>Landing Gear</b><br><input type="checkbox"/> Bending<br><input type="checkbox"/> Centre Not Concentric to O/S<br><input type="checkbox"/> Cracks<br><input type="checkbox"/> Crushed/Crimped<br><input type="checkbox"/> Cuffs<br><input type="checkbox"/> Heat Treat<br><input type="checkbox"/> Inspection Strip in Tube<br><input type="checkbox"/> Ripples in Bend<br><input type="checkbox"/> Torque Waves in Extrusion<br><input type="checkbox"/> Turning Sequence<br><input type="checkbox"/> Wave/Twist in Tube | <b>General</b><br><input type="checkbox"/> Bend<br><input type="checkbox"/> BOM/Route<br><input type="checkbox"/> Broken/Damaged<br><input type="checkbox"/> Burrs<br><input type="checkbox"/> Contamination<br><input type="checkbox"/> Countersink<br><input type="checkbox"/> Cut Too Short<br><input type="checkbox"/> Drill Holes<br><input type="checkbox"/> Drawing<br><input type="checkbox"/> Finish<br><input type="checkbox"/> Folio | <input type="checkbox"/> Grain<br><input type="checkbox"/> Hardware<br><input type="checkbox"/> Inspection Incomplete<br><input type="checkbox"/> Instructions Incomplete/Unclear<br><input type="checkbox"/> Maintenance<br><input type="checkbox"/> Mislabeled<br><input type="checkbox"/> Misread<br><input type="checkbox"/> Offset<br><input type="checkbox"/> Out of Calibration<br><input type="checkbox"/> Out of Sequence<br><input type="checkbox"/> Outside Dimensions | <input type="checkbox"/> Ovalized<br><input type="checkbox"/> Over/Under tolerance<br><input type="checkbox"/> Part Incorrect<br><input type="checkbox"/> Part Lost/Missing<br><input type="checkbox"/> Part Moved<br><input type="checkbox"/> Positioned Wrong<br><input type="checkbox"/> Power Loss/Surge<br><br><input type="checkbox"/> Pressure/Forced<br><input type="checkbox"/> Temperature/Cure<br><input type="checkbox"/> Weld<br><input type="checkbox"/> Wrong Stock Pulled<br><br><input type="checkbox"/> Other |
|---|---|---|---|

# Work Order ID 94343

December-10-12 12:36:21 PM

**\*94343\***

Page 3

Item ID: D206-667-247TRN

Accept

**\*N900040100\***

Setup Start **\*NS1\***

Revision ID:

Stop **\*NS2\***

Item Name: Crosstube Assembly, Mid Aft

Start Date: 10/12/2012 Start Qty: 1.00

**\*1\***

Cust Item ID:

Required Date: 24/12/2012 Req'd Qty: 1.00

**\*1\***

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run Start **\*NR1\***

QC:

Date:

SPC (Y/N):

Date:

Stop **\*NR2\***

| Sequence ID/<br>Work Center ID | Operation<br>Description                                 | Set Up/<br>Run Hours | Tool ID | Tool # | Plan<br>Code | Accept<br>Qty | Reject<br>Qty | Reject<br>Number | Insp.<br>Stamp |
|--------------------------------|--|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
| 150                            |  | 0.00                 |         |        |              |               |               |                  |                |
| <b>*150*</b>                   |  |                      |         |        |              |               |               |                  |                |
| HandFXtube                     | Memo   | 0.00                 |         |        |              |               |               |                  |                |
| Hand Finishing Crosstubes      | 1- PRESSURE WASH X-TUBE INSIDE AND OUT                   |                      |         |        |              |               |               |                  |                |
|                                | 2- ACID ETCH X-TUBE INSIDE AND OUT. USE RED SCOTCH BRITE |                      |         |        |              |               |               |                  |                |
| 160                            | QC5- Inspect part completeness to step on W/O            | 0.00                 |         |        |              |               |               |                  |                |
| <b>*160*</b>                   |  |                      |         |        |              |               |               |                  |                |
| QC                             | Memo   | 0.00                 |         |        |              |               |               |                  |                |
| Quality Control                |  |                      |         |        |              |               |               |                  |                |
| 170                            | Packaging  | 0.00                 |         |        |              |               |               |                  |                |
| <b>*170*</b>                   |  |                      |         |        |              |               |               |                  |                |
| Packaging                      | Memo   | 0.00                 |         |        |              |               |               |                  |                |
| Packaging                      | Identify and stock in kanban rack                        |                      |         |        |              |               |               |                  |                |
|                                | Location: <u>LG</u>                                      |                      |         |        |              |               |               |                  |                |

*Rm* 12-12-21

*DAS* 12/12/21

*Rm* 12-12-28

NCR: Yes / No

## WORK ORDER NON-CONFORMANCE / UPDATE

DQA: \_\_\_\_\_ Date: \_\_\_\_\_

QA Closed: \_\_\_\_\_ Date: \_\_\_\_\_

|  |   |   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____<br><br>Part No. _____<br><br>NCR No. _____ | <b>DISPOSITION</b><br><br>Rework <input type="checkbox"/><br>Scrap <input type="checkbox"/><br>Use-as-is <input type="checkbox"/><br>Work Order Update <input type="checkbox"/> | <b>AGAINST DEPARTMENT/PROCESS</b><br><br><table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/>   | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> |  |
| Skid-tube <input type="checkbox"/>                           | Crosstube <input type="checkbox"/>  | Water Jet <input type="checkbox"/>  | Engineering <input type="checkbox"/> |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Machining <input type="checkbox"/>                           | Small Fab <input type="checkbox"/>  | Prod. Eng. Coord. <input type="checkbox"/>  | Quality <input type="checkbox"/>     |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Thermoforming <input type="checkbox"/>                       | Finishing <input type="checkbox"/>  | Rec/Store/Packaging <input type="checkbox"/>  | Other <input type="checkbox"/>       |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Large Fab <input type="checkbox"/>                           | Composite <input type="checkbox"/>  | Supplier <input type="checkbox"/>   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |

| Root Cause                             | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Equip/Tooling <input type="checkbox"/> |      |      |     |   |                   |                    |             |              |              |
| Operator <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Material <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Setup <input type="checkbox"/>         |      |      |     |   |                   |                    |             |              |              |
| Other <input type="checkbox"/>         |      |      |     |   |                   |                    |             |              |              |
| Process <input type="checkbox"/>       |      |      |     |   |                   |                    |             |              |              |
| Supplier <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Training <input type="checkbox"/>      |      |      |     |   |                   |                    |             |              |              |
| Unapproved <input type="checkbox"/>    |      |      |     |   |                   |                    |             |              |              |

### FAULT CATEGORY

|  |   |   |  |   |
|--|---|---|--|---|
| <b>Landing Gear</b><br><input type="checkbox"/> Bending<br><input type="checkbox"/> Centre Not Concentric to O/S<br><input type="checkbox"/> Cracks<br><input type="checkbox"/> Crushed/Crimped.<br><input type="checkbox"/> Cuffs<br><input type="checkbox"/> Heat Treat<br><input type="checkbox"/> Inspection Strip in Tube<br><input type="checkbox"/> Ripples in Bend<br><input type="checkbox"/> Torque Waves in Extrusion<br><input type="checkbox"/> Turning Sequence<br><input type="checkbox"/> Wave/Twist in Tube | <b>General</b><br><input type="checkbox"/> Bend<br><input type="checkbox"/> BOM/Route<br><input type="checkbox"/> Broken/Damaged<br><input type="checkbox"/> Burrs<br><input type="checkbox"/> Contamination<br><input type="checkbox"/> Countersink<br><input type="checkbox"/> Cut Too Short<br><input type="checkbox"/> Drill Holes<br><input type="checkbox"/> Drawing<br><input type="checkbox"/> Finish<br><input type="checkbox"/> Folio | <input type="checkbox"/> Grain<br><input type="checkbox"/> Hardware<br><input type="checkbox"/> Inspection Incomplete<br><input type="checkbox"/> Instructions Incomplete/Unclear<br><input type="checkbox"/> Maintenance<br><input type="checkbox"/> Mislabeled<br><input type="checkbox"/> Misread<br><input type="checkbox"/> Offset<br><input type="checkbox"/> Out of Calibration<br><input type="checkbox"/> Out of Sequence<br><input type="checkbox"/> Outside Dimensions | <input type="checkbox"/> Ovalized<br><input type="checkbox"/> Over/Under tolerance<br><input type="checkbox"/> Part Incorrect<br><input type="checkbox"/> Part Lost/Missing<br><input type="checkbox"/> Part Moved<br><input type="checkbox"/> Positioned Wrong<br><input type="checkbox"/> Power Loss/Surge | <input type="checkbox"/> Pressure/Forced<br><input type="checkbox"/> Temperature/Cure<br><input type="checkbox"/> Weld<br><input type="checkbox"/> Wrong Stock Pulled<br><br><input type="checkbox"/> Other |
|--|---|---|--|---|

**Work Order ID 94343**

December-10-12 12:36:21 PM

**\*94343\***

Page 4

Item ID: D206-667-247TRN

Accept

**\*N900040100\***Setup Start **\*NS1\***

Revision ID:

Stop **\*NS2\***

Item Name: Crosstube Assembly, Mid Aft

Start Date: 10/12/2012 Start Qty: 1.00

**\*1\***

Cust Item ID:

Required Date: 24/12/2012 Req'd Qty: 1.00

**\*1\***

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run Start **\*NR1\***

QC:

Date:

SPC (Y/N):

Date:

Stop **\*NR2\***Sequence ID/  
Work Center IDOperation  
DescriptionSet Up/  
Run Hours

Tool ID

Tool #

Plan  
CodeAccept  
QtyReject  
QtyReject  
NumberInsp.  
Stamp

180

QC21- Final Inspection - Work Order Release

0.00

**\*180\***

QC

Memo

0.00

Quality Control

13/1/10

U121231

NCR: Yes / No

**WORK ORDER NON-CONFORMANCE / UPDATE**

DQA: \_\_\_\_\_ Date: \_\_\_\_\_

QA Closed: \_\_\_\_\_ Date: \_\_\_\_\_

|  |   |   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____<br><br>Part No. _____<br><br>NCR No. _____ | <b>DISPOSITION</b><br><br>Rework <input type="checkbox"/><br>Scrap <input type="checkbox"/><br>Use-as-is <input type="checkbox"/><br>Work Order Update <input type="checkbox"/> | <b>AGAINST DEPARTMENT/PROCESS</b><br><br><table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/>   | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> |  |
| Skid-tube <input type="checkbox"/>                           | Crosstube <input type="checkbox"/>  | Water Jet <input type="checkbox"/>  | Engineering <input type="checkbox"/> |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Machining <input type="checkbox"/>                           | Small Fab <input type="checkbox"/>  | Prod. Eng. Coord. <input type="checkbox"/>  | Quality <input type="checkbox"/>     |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Thermoforming <input type="checkbox"/>                       | Finishing <input type="checkbox"/>  | Rec/Store/Packaging <input type="checkbox"/>  | Other <input type="checkbox"/>       |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Large Fab <input type="checkbox"/>                           | Composite <input type="checkbox"/>  | Supplier <input type="checkbox"/>   |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |

| Root Cause    | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data      |      |      |     |   |                   |                    |             |              |              |
| Equip/Tooling |      |      |     |   |                   |                    |             |              |              |
| Operator      |      |      |     |   |                   |                    |             |              |              |
| Material      |      |      |     |   |                   |                    |             |              |              |
| Setup         |      |      |     |   |                   |                    |             |              |              |
| Other         |      |      |     |   |                   |                    |             |              |              |
| Process       |      |      |     |   |                   |                    |             |              |              |
| Supplier      |      |      |     |   |                   |                    |             |              |              |
| Training      |      |      |     |   |                   |                    |             |              |              |
| Unapproved    |      |      |     |   |                   |                    |             |              |              |

**FAULT CATEGORY**

| Landing Gear  | General                                 | Other  |
|---|---|--|
| <input type="checkbox"/> Bending                      | <input type="checkbox"/> Bend           | <input type="checkbox"/> Grain                           |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route      | <input type="checkbox"/> Hardware                        |
| <input type="checkbox"/> Cracks                       | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete           |
| <input type="checkbox"/> Crushed/Crimped              | <input type="checkbox"/> Burrs          | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs                        | <input type="checkbox"/> Contamination  | <input type="checkbox"/> Maintenance                     |
| <input type="checkbox"/> Heat Treat                   | <input type="checkbox"/> Countersink    | <input type="checkbox"/> Mislabeled                      |
| <input type="checkbox"/> Inspection Strip in Tube     | <input type="checkbox"/> Cut Too Short  | <input type="checkbox"/> Misread                         |
| <input type="checkbox"/> Ripples in Bend              | <input type="checkbox"/> Drill Holes    | <input type="checkbox"/> Offset                          |
| <input type="checkbox"/> Torque Waves in Extrusion    | <input type="checkbox"/> Drawing        | <input type="checkbox"/> Out of Calibration              |
| <input type="checkbox"/> Turning Sequence             | <input type="checkbox"/> Finish         | <input type="checkbox"/> Out of Sequence                 |
| <input type="checkbox"/> Wave/Twist in Tube           | <input type="checkbox"/> Folio          | <input type="checkbox"/> Outside Dimensions              |
|   |   | <input type="checkbox"/> Ovalized                        |
|   |   | <input type="checkbox"/> Over/Under tolerance            |
|   |   | <input type="checkbox"/> Part Incorrect                  |
|   |   | <input type="checkbox"/> Part Lost/Missing               |
|   |   | <input type="checkbox"/> Part Moved                      |
|   |   | <input type="checkbox"/> Positioned Wrong                |
|   |   | <input type="checkbox"/> Power Loss/Surge                |
|   |   | <input type="checkbox"/> Pressure/Forced                 |
|   |   | <input type="checkbox"/> Temperature/Cure                |
|   |   | <input type="checkbox"/> Weld                            |
|   |   | <input type="checkbox"/> Wrong Stock Pulled              |
|   |   | <input type="checkbox"/> Other                           |



# Picklist Print

December-10-12 12:36:24 PM

Page 1

Work Order ID: 94343

\*94343\*

Parent Item: D206-667-247TRN

\*D206-667-247TRN\*

Parent Item Name: Crosstube Assembly, Mid Aft

Start Date: 10/12/2012

Required Date: 24/12/2012

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP rev:A 11.01.06 new issue DD verf:EC

| Component Item ID/<br>Item Name | Replacement<br>Item ID | Mfg/<br>Purch | Bin<br>Item | Primary<br>Location | Last<br>Location | Route<br>Seq ID | Unit of<br>Measure | Qty on<br>Hand | Qty per Kit | Total<br>Qty | Qty<br>Issued | Date<br>Issued | Status |
|---------------------------------|------------------------|---------------|-------------|---------------------|------------------|-----------------|--------------------|----------------|-------------|--------------|---------------|----------------|--------|
| D6004-115                       |                        | Manufactured  | No          |                     |                  | 100             | Each               | 53.0000        | 1           | 1            |               |                |        |

**D6004-115**  
Crosstube Material

\*\*

Location

Loc Qty

Loc Code

LG015

53

34685

1

**69795**

15

75636

37

1 mm.c 12/12/12

NCR: Yes / No

**WORK ORDER NON-CONFORMANCE / UPDATE**

DQA: \_\_\_\_\_ Date: \_\_\_\_\_

QA Closed: \_\_\_\_\_ Date: \_\_\_\_\_

|  |   |  |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
|--|---|--|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____<br><br>Part No. _____<br><br>NCR No. _____ | <b>DISPOSITION</b><br><br>Rework <input type="checkbox"/><br>Scrap <input type="checkbox"/><br>Use-as-is <input type="checkbox"/><br>Work Order Update <input type="checkbox"/> | <b>AGAINST DEPARTMENT/PROCESS</b><br><br><table style="width:100%; border: none;"> <tr> <td style="width:33%;">Skid-tube <input type="checkbox"/></td> <td style="width:33%;">Crosstube <input type="checkbox"/></td> <td style="width:33%;">Water Jet <input type="checkbox"/></td> <td style="width:33%;">Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/>   | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> |  |
| Skid-tube <input type="checkbox"/>                           | Crosstube <input type="checkbox"/>  | Water Jet <input type="checkbox"/>   | Engineering <input type="checkbox"/> |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Machining <input type="checkbox"/>                           | Small Fab <input type="checkbox"/>  | Prod. Eng. Coord. <input type="checkbox"/>   | Quality <input type="checkbox"/>     |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Thermoforming <input type="checkbox"/>                       | Finishing <input type="checkbox"/>  | Rec/Store/Packaging <input type="checkbox"/>   | Other <input type="checkbox"/>       |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |
| Large Fab <input type="checkbox"/>                           | Composite <input type="checkbox"/>  | Supplier <input type="checkbox"/>  |                                      |                                    |                                    |                                      |                                    |                                    |  |                                  |  |                                    |  |                                |                                    |                                    |                                   |  |

| Root Cause    | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data      |      |      |     |   |                   |                    |             |              |              |
| Equip/Tooling |      |      |     |   |                   |                    |             |              |              |
| Operator      |      |      |     |   |                   |                    |             |              |              |
| Material      |      |      |     |   |                   |                    |             |              |              |
| Setup         |      |      |     |   |                   |                    |             |              |              |
| Other         |      |      |     |   |                   |                    |             |              |              |
| Process       |      |      |     |   |                   |                    |             |              |              |
| Supplier      |      |      |     |   |                   |                    |             |              |              |
| Training      |      |      |     |   |                   |                    |             |              |              |
| Unapproved    |      |      |     |   |                   |                    |             |              |              |

**FAULT CATEGORY**

| Landing Gear  | General                                 | Other  |
|---|---|--|
| <input type="checkbox"/> Bending                      | <input type="checkbox"/> Bend           | <input type="checkbox"/> Grain                           |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route      | <input type="checkbox"/> Hardware                        |
| <input type="checkbox"/> Cracks                       | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete           |
| <input type="checkbox"/> Crushed/Crimped              | <input type="checkbox"/> Burrs          | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs                        | <input type="checkbox"/> Contamination  | <input type="checkbox"/> Maintenance                     |
| <input type="checkbox"/> Heat Treat                   | <input type="checkbox"/> Countersink    | <input type="checkbox"/> Mislabeled                      |
| <input type="checkbox"/> Inspection Strip in Tube     | <input type="checkbox"/> Cut Too Short  | <input type="checkbox"/> Misread                         |
| <input type="checkbox"/> Ripples in Bend              | <input type="checkbox"/> Drill Holes    | <input type="checkbox"/> Offset                          |
| <input type="checkbox"/> Torque Waves in Extrusion    | <input type="checkbox"/> Drawing        | <input type="checkbox"/> Out of Calibration              |
| <input type="checkbox"/> Turning Sequence             | <input type="checkbox"/> Finish         | <input type="checkbox"/> Out of Sequence                 |
| <input type="checkbox"/> Wave/Twist in Tube           | <input type="checkbox"/> Folio          | <input type="checkbox"/> Outside Dimensions              |
|   |   | <input type="checkbox"/> Ovalized                        |
|   |   | <input type="checkbox"/> Over/Under tolerance            |
|   |   | <input type="checkbox"/> Part Incorrect                  |
|   |   | <input type="checkbox"/> Part Lost/Missing               |
|   |   | <input type="checkbox"/> Part Moved                      |
|   |   | <input type="checkbox"/> Positioned Wrong                |
|   |   | <input type="checkbox"/> Power Loss/Surge                |
|   |   | <input type="checkbox"/> Pressure/Forced                 |
|   |   | <input type="checkbox"/> Temperature/Cure                |
|   |   | <input type="checkbox"/> Weld                            |
|   |   | <input type="checkbox"/> Wrong Stock Pulled              |
|   |   | <input type="checkbox"/> Other                           |


|   |  |                     |                 |
|---|--|---------------------|-----------------|
| <b>DART AEROSPACE LTD</b>                         |  | <b>Work Order:</b>  | 94343           |
| <b>Description:</b> Crosstube Assembly, Mid Aft   |  | <b>Part Number:</b> | D206-667-247TRN |
| <b>Inspection Dwg:</b> D206-667-247 <b>Rev:</b> A |  | <b>Page 1 of 2</b>  |                 |

### FIRST ARTICLE INSPECTION CHECKLIST

|        | Inspection Sheet Drawing Dimension | Tolerance     | Actual Dimension | Accept | Reject | Method of Inspection | Comments |
|--------|------------------------------------|---------------|------------------|--------|--------|----------------------|----------|
| SIDE A | 2.490                              | +0.005/-0.000 | 2.492            | /      |        | vern                 | CNC-08   |
|        | 2.025                              | +0.005/-0.000 | 2.028            | /      |        | ↓                    |          |
|        | 2.079                              | +0.005/-0.000 | 2.083            | /      |        |                      |          |
|        | 2.145                              | +0.005/-0.000 | 2.150            | /      |        |                      |          |
|        | 2.209                              | +0.005/-0.000 | 2.214            | /      |        |                      |          |
|        | 2.287                              | +0.005/-0.000 | 2.292            | /      |        |                      |          |
|        | 2.363                              | +0.005/-0.000 | 2.368            | /      |        | ↓                    |          |
|        | 0.200                              | +/-0.010      | 0.200            | /      |        | vern                 | CNC-08   |
|        | R0.063                             | +/-0.010      | 0.063            | /      |        | RG                   |          |
|        | R2.00                              | +/-0.010      | 2.00             | /      |        | "                    |          |
|        | R0.063                             | +/-0.010      | 0.063            | /      |        | "                    |          |
|        | 4.438                              | +/-0.010      | 4.438            | /      |        | vern                 | CNC-08   |
|        |                                    |               |                  |        |        |                      |          |
|        |                                    |               |                  |        |        |                      |          |
| SIDE B | 2.490                              | +0.005/-0.000 | 2.492            | /      |        | vern                 | CNC-08   |
|        | 2.025                              | +0.005/-0.000 | 2.028            | /      |        | ↓                    |          |
|        | 2.079                              | +0.005/-0.000 | 2.083            | /      |        |                      |          |
|        | 2.145                              | +0.005/-0.000 | 2.150            | /      |        |                      |          |
|        | 2.209                              | +0.005/-0.000 | 2.213            | /      |        |                      |          |
|        | 2.287                              | +0.005/-0.000 | 2.291            | /      |        |                      |          |
|        | 2.363                              | +0.005/-0.000 | 2.368            | /      |        | ↓                    |          |
|        | 0.200                              | +/-0.010      | 0.206            | /      |        | vern                 | CNC-08   |
|        | R0.063                             | +/-0.010      | 0.063            | /      |        | RG                   |          |
|        | R2.00                              | +/-0.010      | 2.00             | /      |        | "                    |          |
|        | R0.063                             | +/-0.010      | 0.063            | /      |        | "                    |          |
|        | 4.438                              | +/-0.010      | 4.438            | /      |        | vern                 | CNC-08   |
|        |                                    |               |                  |        |        |                      |          |
|        |                                    |               |                  |        |        |                      |          |
|        | 99.76                              | +/-0.020      | 99.75            | /      |        | tape                 | LG-15    |

|   |                                     |
|---|-------------------------------------|
| <b>DART AEROSPACE LTD</b>                         | <b>Work Order:</b> 94343            |
| <b>Description:</b> Crosstube Assembly, Mid Aft   | <b>Part Number:</b> D206-667-247TRN |
| <b>Inspection Dwg:</b> D206-667-247 <b>Rev:</b> A | <b>Page 2 of 2</b>                  |

### WALL THICKNESS MEASUREMENT

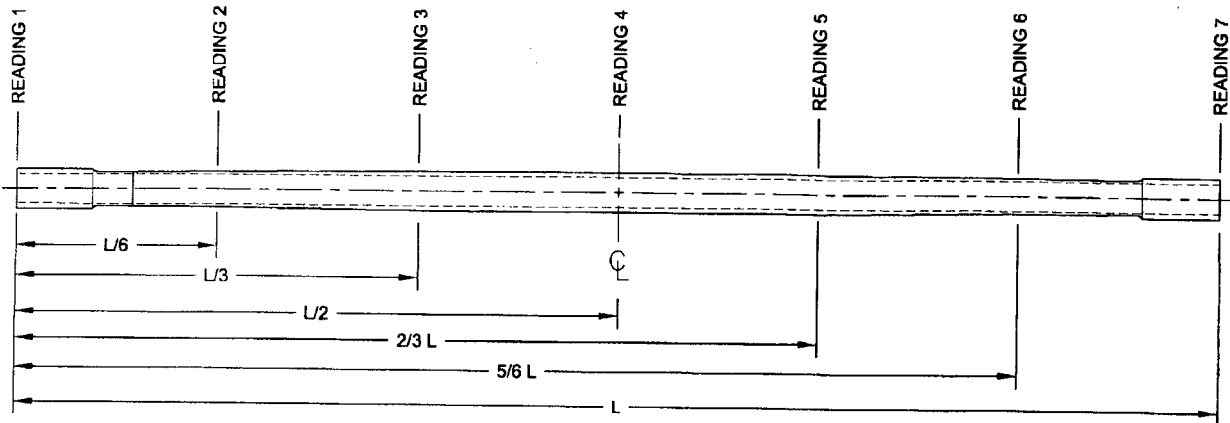

| Location             | WALL THICKNESS MEASUREMENT (IN) |      |      |      | Deviation<br>$\Delta w$<br>(max-min) | TOLERANCE |
|----------------------|---------------------------------|------|------|------|--------------------------------------|-----------|
|                      | w1                              | w2   | w3   | w4   |                                      |           |
| READING 1<br>L= 0"   | .343                            | .351 | .366 | .357 | .023                                 | 0.045"    |
| READING 2<br>L= 17   | .146                            | .159 | .172 | .160 | .026                                 |           |
| READING 3<br>L= 23   | .228                            | .243 | .255 | .239 | .027                                 |           |
| READING 4<br>L= 49   | .349                            | .356 | .364 | .355 | .015                                 |           |
| READING 5<br>L= 23   | .231                            | .244 | .248 | .234 | .017                                 |           |
| READING 6<br>L= 11   | .148                            | .155 | .165 | .154 | .017                                 |           |
| READING 7<br>L= Cuff | .344                            | .348 | .363 | .355 | .019                                 |           |

#### Calibration Result

Actual Block Thickness: 100 .500

Sitescan 250 Measured Thickness: 100 .500

|                           |                       |                              |
|---------------------------|-----------------------|------------------------------|
| <b>Measured by:</b> M.M.C | <b>Audited by:</b> JW | <b>Preliminary Approval:</b> |
| <b>Date:</b> 12/12/17     | <b>Date:</b> 12-12-17 | <b>Date:</b>                 |

| Rev | Date     | Change                    | Revised by | Approved |
|-----|----------|---------------------------|------------|----------|
| A   | 11.06.21 | New Issue                 | KJ         |          |
| B   | 12.02.02 | Dimension 4.438 was 4.500 | KJ         |          |
| C   | 12.06.01 | Wall thickness form added | KJ         |          |

| Item | Qty  | Part Number    | Description  |
|------|------|----------------|--|
|      | -247 |                |  |
| 1    | X    | D206-667-247   | CROSSTUBE ASSEMBLY (206L MID AFT)  |
| 2    | 1    | D6004-115      | CROSSTUBE  |
| 3    | 2    | D2873-043      | NUT PLATE  |
| 4    | 2    | D2873-045      | NUT PLATE  |
| 5    | 2    | D2892-1        | SUPPORT  |
| 6    | 4    | D3595-063-450  | RUBBER CUSHION   |
| 7    | 4    | MS21920-22     | CLAMP  |
| 8    | 14   | MS20601AD4W10  | RIVET (OR NAS9302B-4-10)   |
| 9    | A/R  | MAGNOBOND 6398 | ROCKWELL SPECIFICATION RBO-120-023<br>ADHESIVE (TEXTRON/BELL SPEC. 299-<br>947-100, TYPE II, CLASS 2 ADHESIVE) |

#### GENERAL NOTES:

- 1) MATERIAL: MANUFACTURED FROM D6004-115  
FINISHED LENGTH = 99.76±0.020
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1  
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2  
PAINT OUTSIDE PER DART QSI 005 4.2
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED.
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- 6) IDENTIFICATION: SCRIBE DART PART NUMBER "D206-667-247" AND BATCH NUMBER ON INSIDE OF CUFF PER DART QSI 044 6.4 (VIBRATING STYLUS).
- 7) WEIGHT: 21.1 lbs (-607 = 17.7 lbs)
- 8) PART IS SYMMETRIC ABOUT CENTERLINE.
- 9) RUN CUTTER OFF PART WHERE INDICATED. BLEND OUT EDGE LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH.
- 10) BEND PROGRESSIVELY WITH A MINIMUM OF 10 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 11) LIQUID PENETRANT INSPECT OUTSIDE SURFACE OF CROSSTUBE PER QSI 038.
- 12) INSTALL D2892-1 SUPPORT USING 0.03" TO 0.06" THICK LAYER OF MAGNOBOND 6398 PER QSI 015. LET CURE FOR 12 HOURS AFTER INSTALLATION AND PRIOR TO PACKAGING.
- 13) INSTALL MS21920-22 CLAMPS WITH D3595-063-450 RUBBER CUSHIONS TO SECURE THE D2892-1 SUPPORT ON TOP SIDE OF THE CROSSTUBE. ENSURE CLAMP MECHANISMS ARE LOCATED ON CROSSTUBE SUPPORTS.
- 14) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.
- 15) TORQUE CLAMPS 80 TO 100 IN.-LB. ENSURE AT LEAST 1.5 THREADS ARE SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING.

DEO ATTACHED

BCO #11-615  
11.07.28

UNDER REVIEW

4/11/08 13

RELEASED  
2011-05-24

UNCO  
SUT

10-94343 MCT  
12-12-10

|            |             |    |          |
|------------|-------------|----|----------|
| A          | NEW ISSUE   | CP | 10.12.23 |
| REV.       | DESCRIPTION | BY | DATE     |
| DESIGN     |             |    |          |
| DRAWN      |             |    |          |
| CHECKED    |             |    |          |
| MFG. APPR. |             |    |          |
| APPROVED   |             |    |          |
| DE APPR.   |             |    |          |
| DATE       | 10.12.23    |    |          |


**DART AEROSPACE LTD**  
HAWKESBURY, ONTARIO, CANADA

DRAWING NO. D206-667-247  
REV. A  
SHEET 1 OF 4

TITLE  
CROSSTUBE ASSY (206L MID AFT)  
SCALE  
NTS

COPYRIGHT © 2016 BY DART AEROSPACE LTD  
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR REPRODUCED IN ANY MANNER WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

94343

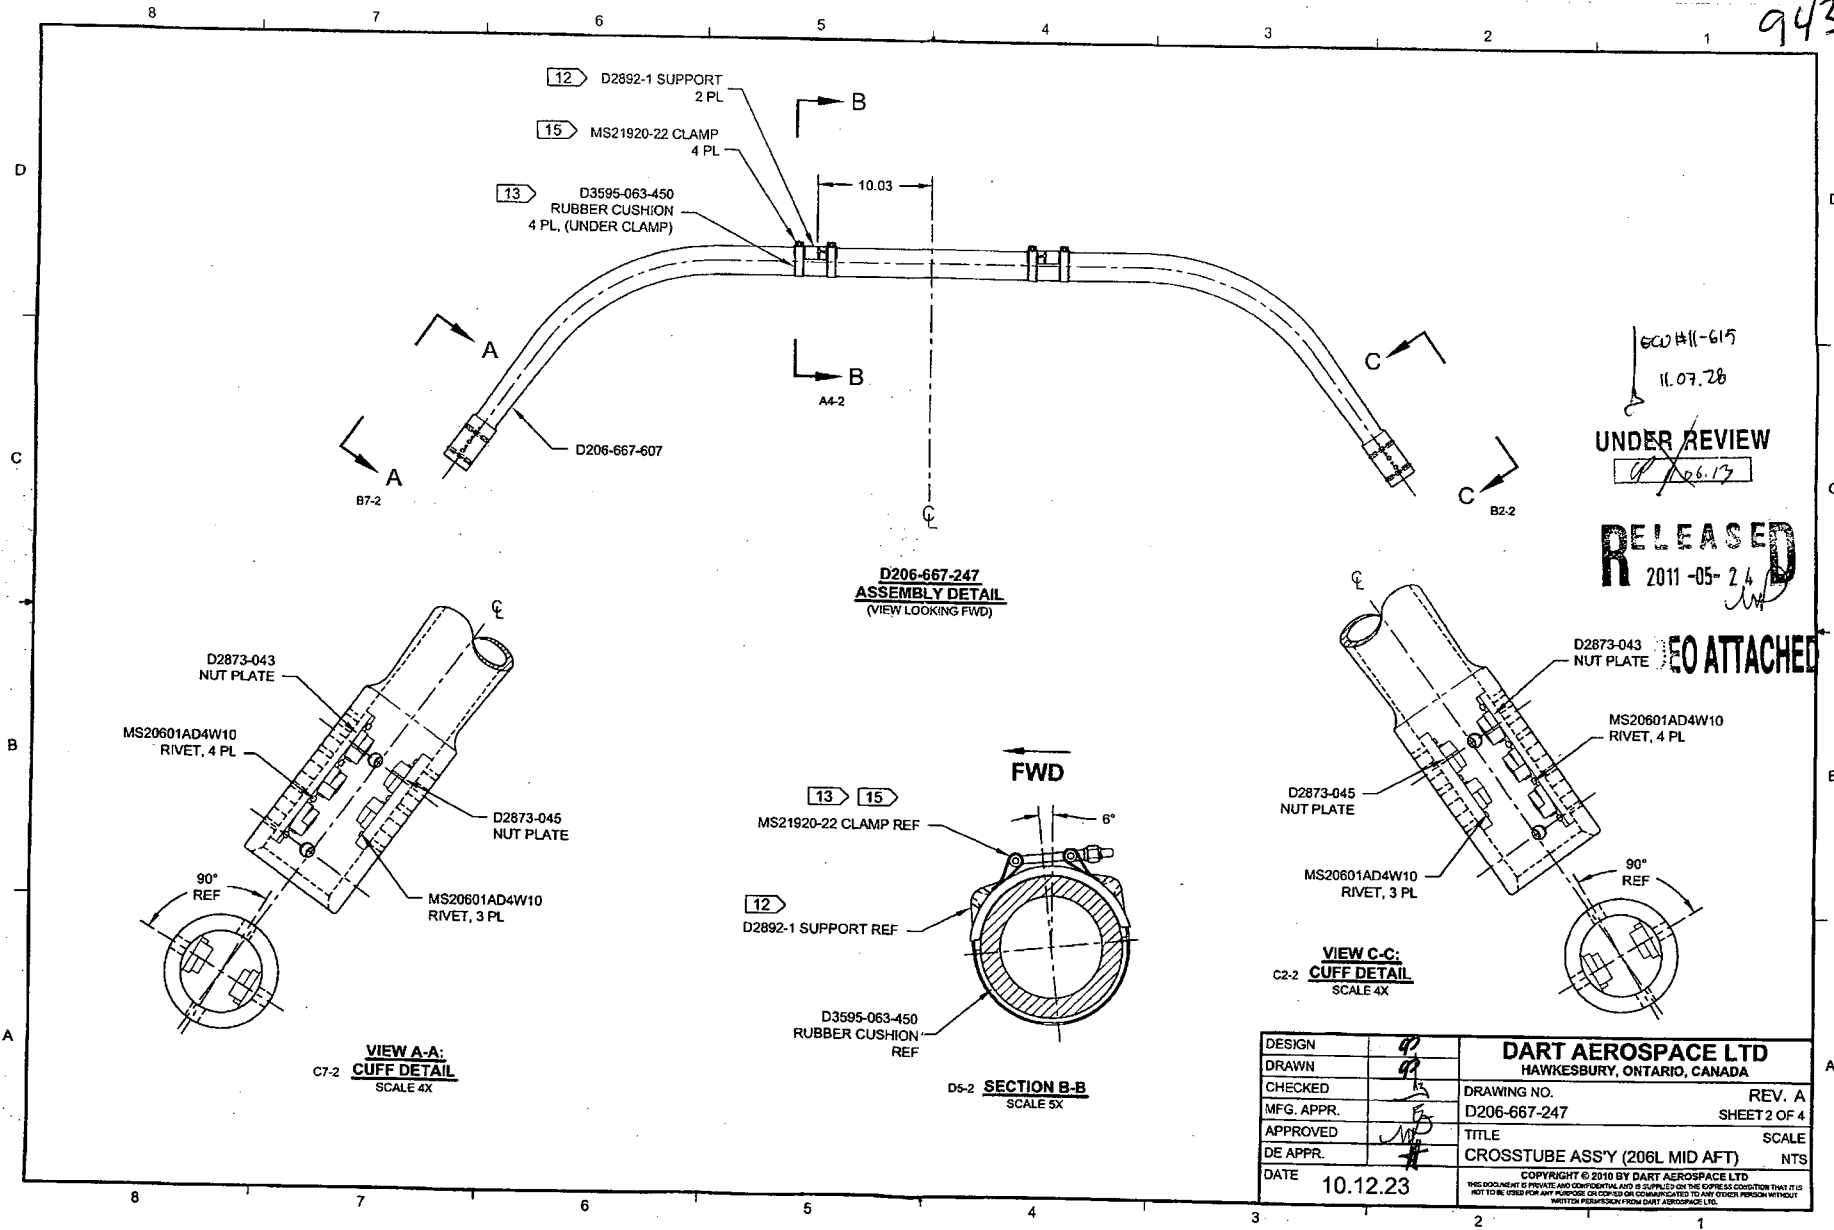

60111-615  
11.07.28  
UNDER REVIEW  
~~06.13~~

**RELEASED**  
2011-05-24  
EO ATTACHED


|            |          |  |              |
|------------|----------|--|--------------|
| DESIGN     |          | <b>DART AEROSPACE LTD</b>  |              |
| DRAWN      |          | HAWKESBURY, ONTARIO, CANADA  |              |
| CHECKED    |          | DRAWING NO.  | REV. A       |
| MFG. APPR. |          | D206-667-247   | SHEET 2 OF 4 |
| APPROVED   |          | TITLE  | SCALE        |
| DE APPR.   |          | CROSSTUBE ASS'Y (206L MID AFT)   | NTS          |
| DATE       | 10.12.23 | <small>COPYRIGHT © 2010 BY DART AEROSPACE LTD<br/>THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR REPRODUCED IN ANY MANNER WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small> |              |

94343

UNDER REVIEW


DEO ATTACHED

RELEASED  
2011-05-24

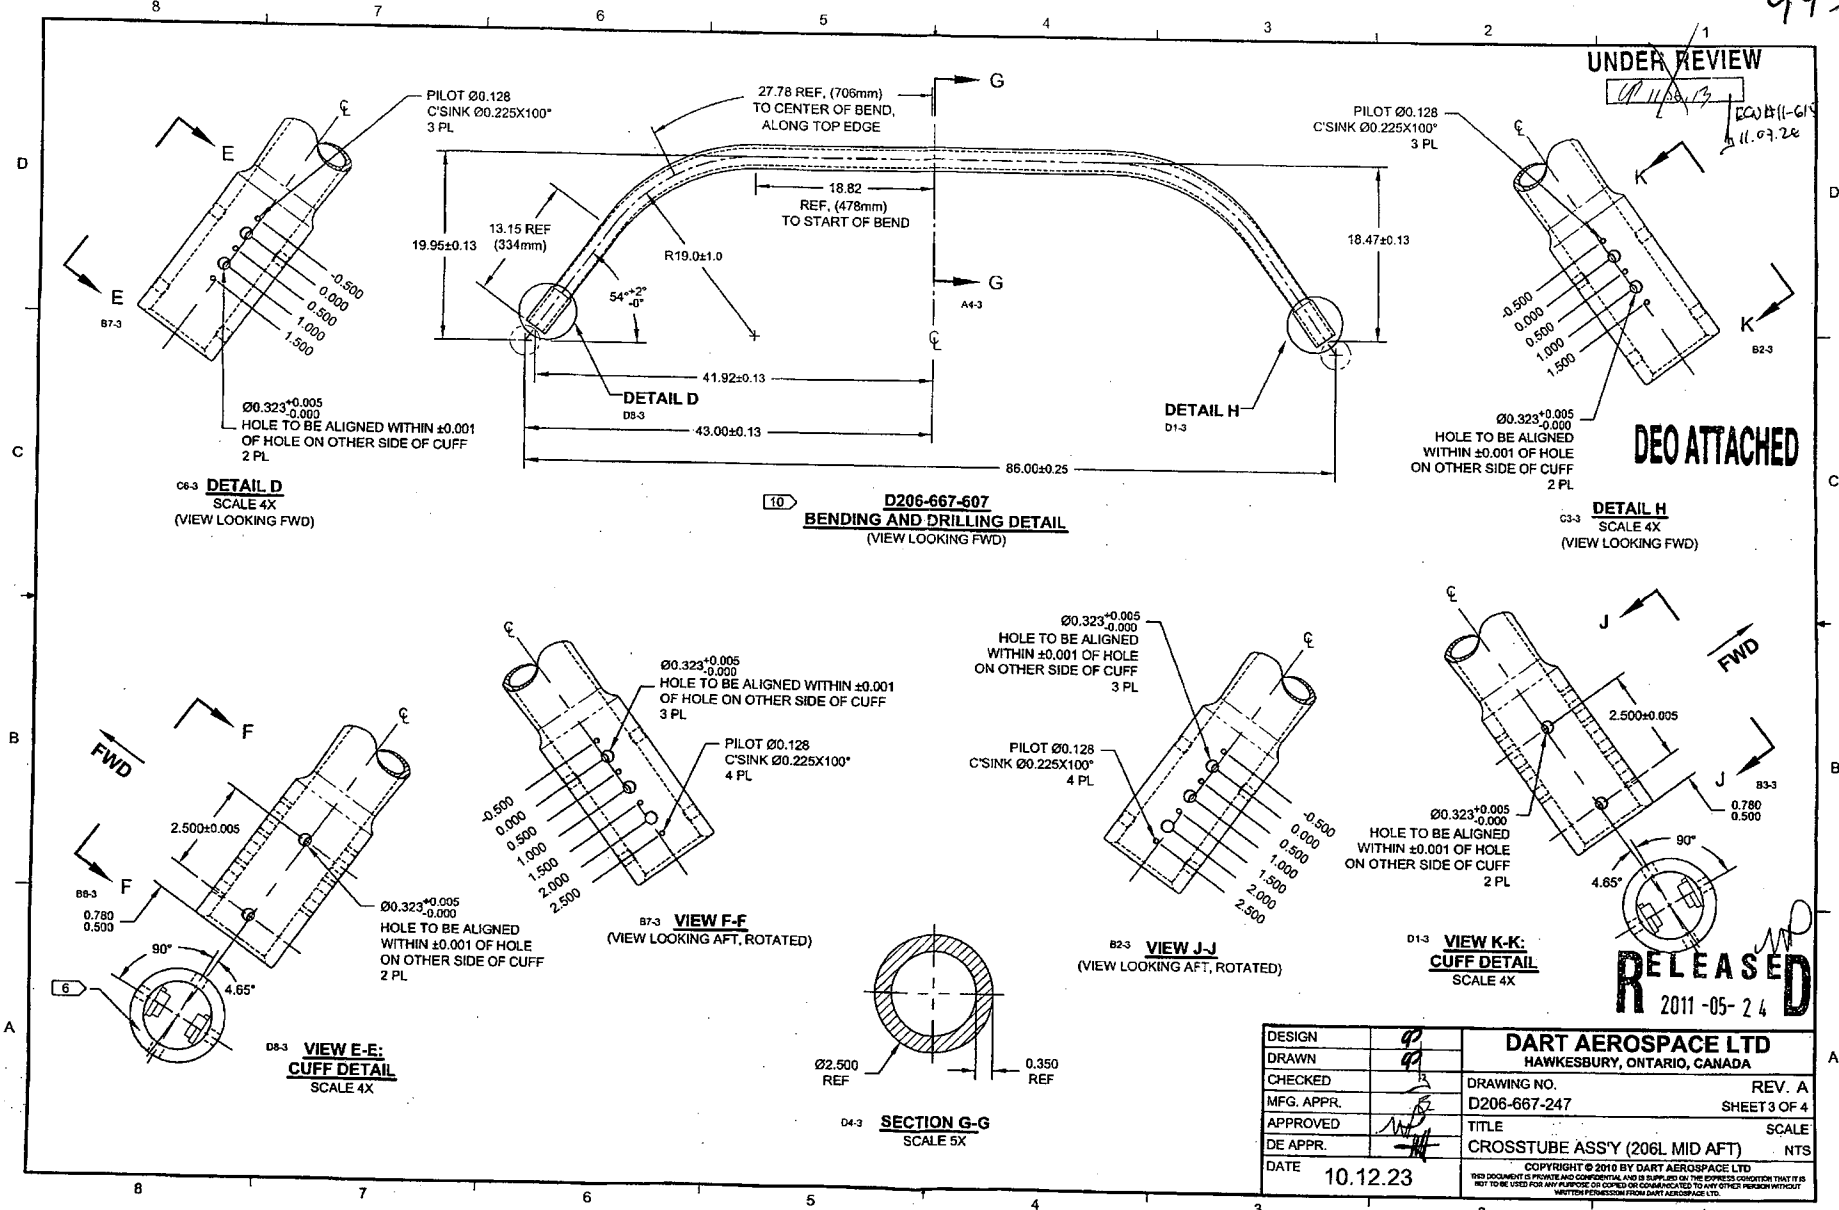


|            |          |  |              |
|------------|----------|--|--------------|
| DESIGN     | 92       | <b>DART AEROSPACE LTD</b>  |              |
| DRAWN      | 92       | HAWKESBURY, ONTARIO, CANADA  |              |
| CHECKED    | 2        | DRAWING NO.  | REV. A       |
| MFG. APPR. | 2        | D206-667-247   | SHEET 3 OF 4 |
| APPROVED   | 2        | TITLE  | SCALE        |
| DE APPR.   | 2        | CROSSTUBE ASS'Y (206L MID AFT)   | NTS          |
| DATE       | 10.12.23 | COPYRIGHT © 2010 BY DART AEROSPACE LTD<br>THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR REPRODUCED IN ANY FORM OR BY ANY MEANS WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD. |              |


94343

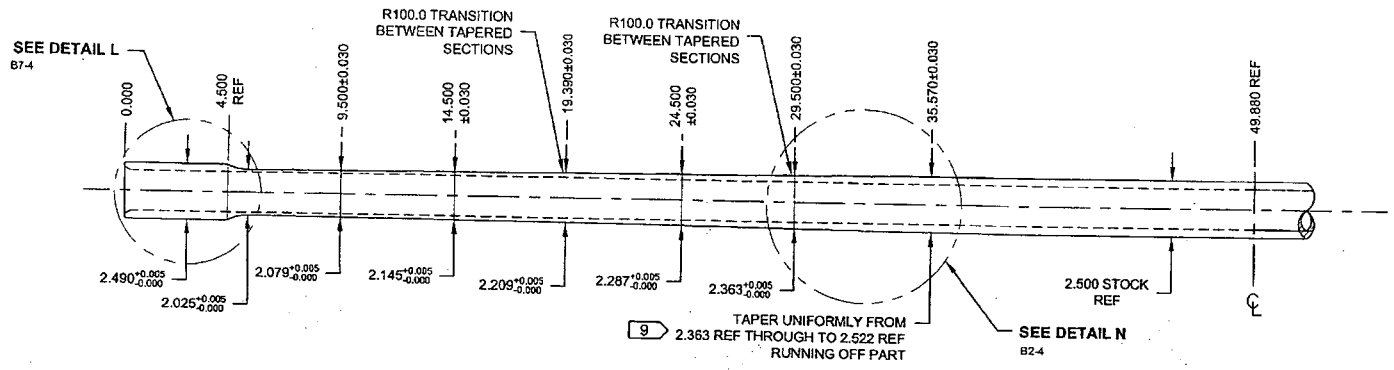


**TURNING DETAIL**

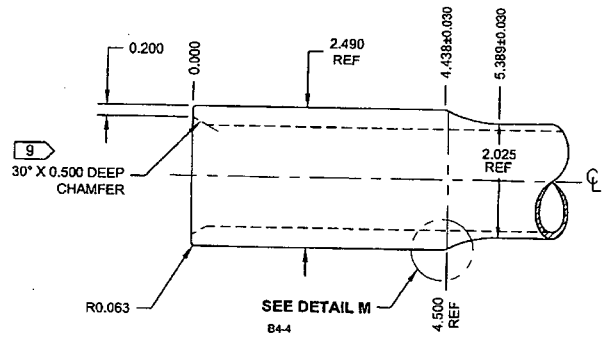

**DETAIL L: CROSSTUBE CUFF**  
SCALE 2.5X

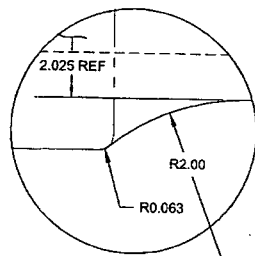

**DETAIL M:  
CUFF TRANSITION**  
NOT TO SCALE

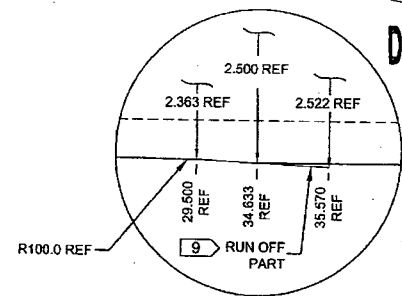

**DETAIL N:  
TAPER RUN-OFF**  
NOT TO SCALE

80044-615  
11.07.28  
**UNDER REVIEW**  
1.06.13

**DEO ATTACHED**

**RELEASED**  
2011-05-24

|            |          |  |              |
|------------|----------|--|--------------|
| DESIGN     |          | <b>DART AEROSPACE LTD</b>  |              |
| DRAWN      |          | HAWKESBURY, ONTARIO, CANADA  |              |
| CHECKED    |          | DRAWING NO.  | REV. A       |
| MFG. APPR. |          | D206-667-247   | SHEET 4 OF 4 |
| APPROVED   |          | TITLE  | SCALE        |
| DE APPR.   |          | CROSSTUBE ASS'Y (206L MID AFT)   | NTS          |
| DATE       | 10.12.23 | <small>COPYRIGHT © 2010 BY DART AEROSPACE LTD<br/>THIS DOCUMENT IS PROPRIETARY AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS<br/>NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT<br/>WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small> |              |



94343

|                             |   |                         |   |  |                                |                           |              |
|-----------------------------|---|-------------------------|---|--|--------------------------------|---------------------------|--------------|
| DRAWING NO.<br>D206-667-247 | TITLE<br>CROSSTUBE ASS'Y (206L MID AFT) | REV. A                  | <b>DART AEROSPACE LTD<br/>ENGINEERING ORDER</b> |  | D.E.O. NO.<br>D206-667-247-A-1 | SHEET NO.<br>SHEET 1 OF 1 | SCALE<br>NTS |
| DRAWN<br><i>JP</i>          | CHECKED<br><i>ASS</i>                   | MFG. APPR.<br><i>AD</i> | APPROVED<br><i>JMP</i>                          |  | DE APPR.<br><i>HA</i>          |                           |              |
| DATE<br>11.07.15            | DATE<br>11.07.20                        | DATE<br>11.07.21        | DATE<br>11/07/21                                |  | DATE<br>11.07.21               |                           |              |

**PURPOSE:**

REPLACE MAGNOBOND WITH PROSEAL.

**CHANGE:**

IS:

| Item | Qty<br>-247 | Part Number     | Description                   |
|------|-------------|-----------------|-------------------------------|
| 9    | A/R         | PROSEAL 890 B-2 | SEALANT, AMS-S-8802 CLASS B-2 |

WAS:

|   |     |                |   |
|---|-----|----------------|---|
| 9 | A/R | MAGNOBOND 6398 | ROCKWELL SPECIFICATION RBO-120-023<br>ADHESIVE (TEXTRON/BELL SPEC. 299-947-100,<br>TYPE II, CLASS 2 ADHESIVE) |
|---|-----|----------------|---|

NOTE 12 & 15, SHEET 1 IS AMENDED AS FOLLOWS:

IS:

- 12) TO INSTALL D2892-1 SUPPORT: ABRASE MATING SURFACE OF SUPPORT AND CROSSTUBE WITH 180-GRIT SANDPAPER AND REMOVE RESIDUE WITH MEK (OR EQUIVALENT). APPLY A 0.04" TO 0.07" THICK LAYER OF PROSEAL 890 CLASS B-2 (OR AMS-S-8802 CLASS B-2) SEALANT TO MATING SURFACE OF SUPPORT.
- 15) TORQUE CLAMPS 80 TO 100 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING. **PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.**

WAS:

- 12) INSTALL D2892-1 SUPPORT USING 0.03" TO 0.06" THICK LAYER OF MAGNOBOND 6398 PER QSI 015. LET CURE FOR 12 HOURS AFTER INSTALLATION AND PRIOR TO PACKAGING.
- 15) TORQUE CLAMPS 80 TO 100 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING.

RELEASED  
2011-07-28  
*W*
